SOUTHERN CROSS ENGINEERING

COAL HANDLING UPGRADE

ID	Task Name
1	**Estimated project commencement.**
2	Project planning and commencement.
3	**Shiploader.**
4	New jetslinger and telescopic chute, supply and site install.
5	Head chute, trolley, cable reelers, cable ladder, & associated works.
6	New cable reeler, supply and install.
7	Electrical upgrade.
8	**Coal Receival. Stockpiling.**
9	Design of conveyors 21, 22, 23, 24.
10	Part demolish workshop building & associated services works.
11	Relocate traintrack NE for access to train unloader area (by others).
12	Civil works for conveyors 21, 22, 23, 24.
13	Supply/manufacture conveyors 21, 22, 23, 24 & associated equipt.
14	Install and commission new conveyors & associated equipment.
15	Electrical installation and services.
16	Civil work for new tracks.
17	Install new tracks (by others)
18	Demolish existing unloader, fuelpad & associated earthworks.
19	New access road, earthworks and services.
20	Demolish workshop building and reinstate services.
21	**Coal Load Out. Reclaiming.**
22	Design of new conveyors 11, 12, 13 & 9A, 9B, 9C.
23	Supply/manufacture conveyors 11, 12, 13, 9A, 9B, 9C.
24	Civil works for conveyors.
25	Install new conveyors and associated equipment.
26	Refurbish existing equipment, extend conveyor 10.
27	Electrical installation and services.
28	**Final Civil Works and Completion.**
29	Stockpile area extension & associated works.
30	Remaining earthworks, drainage, bund, north access road.
31	Lighting and dust suppression.
32	Pumps, wheel wash system.
33	Final electrical and control system.
34	**Project Completion**

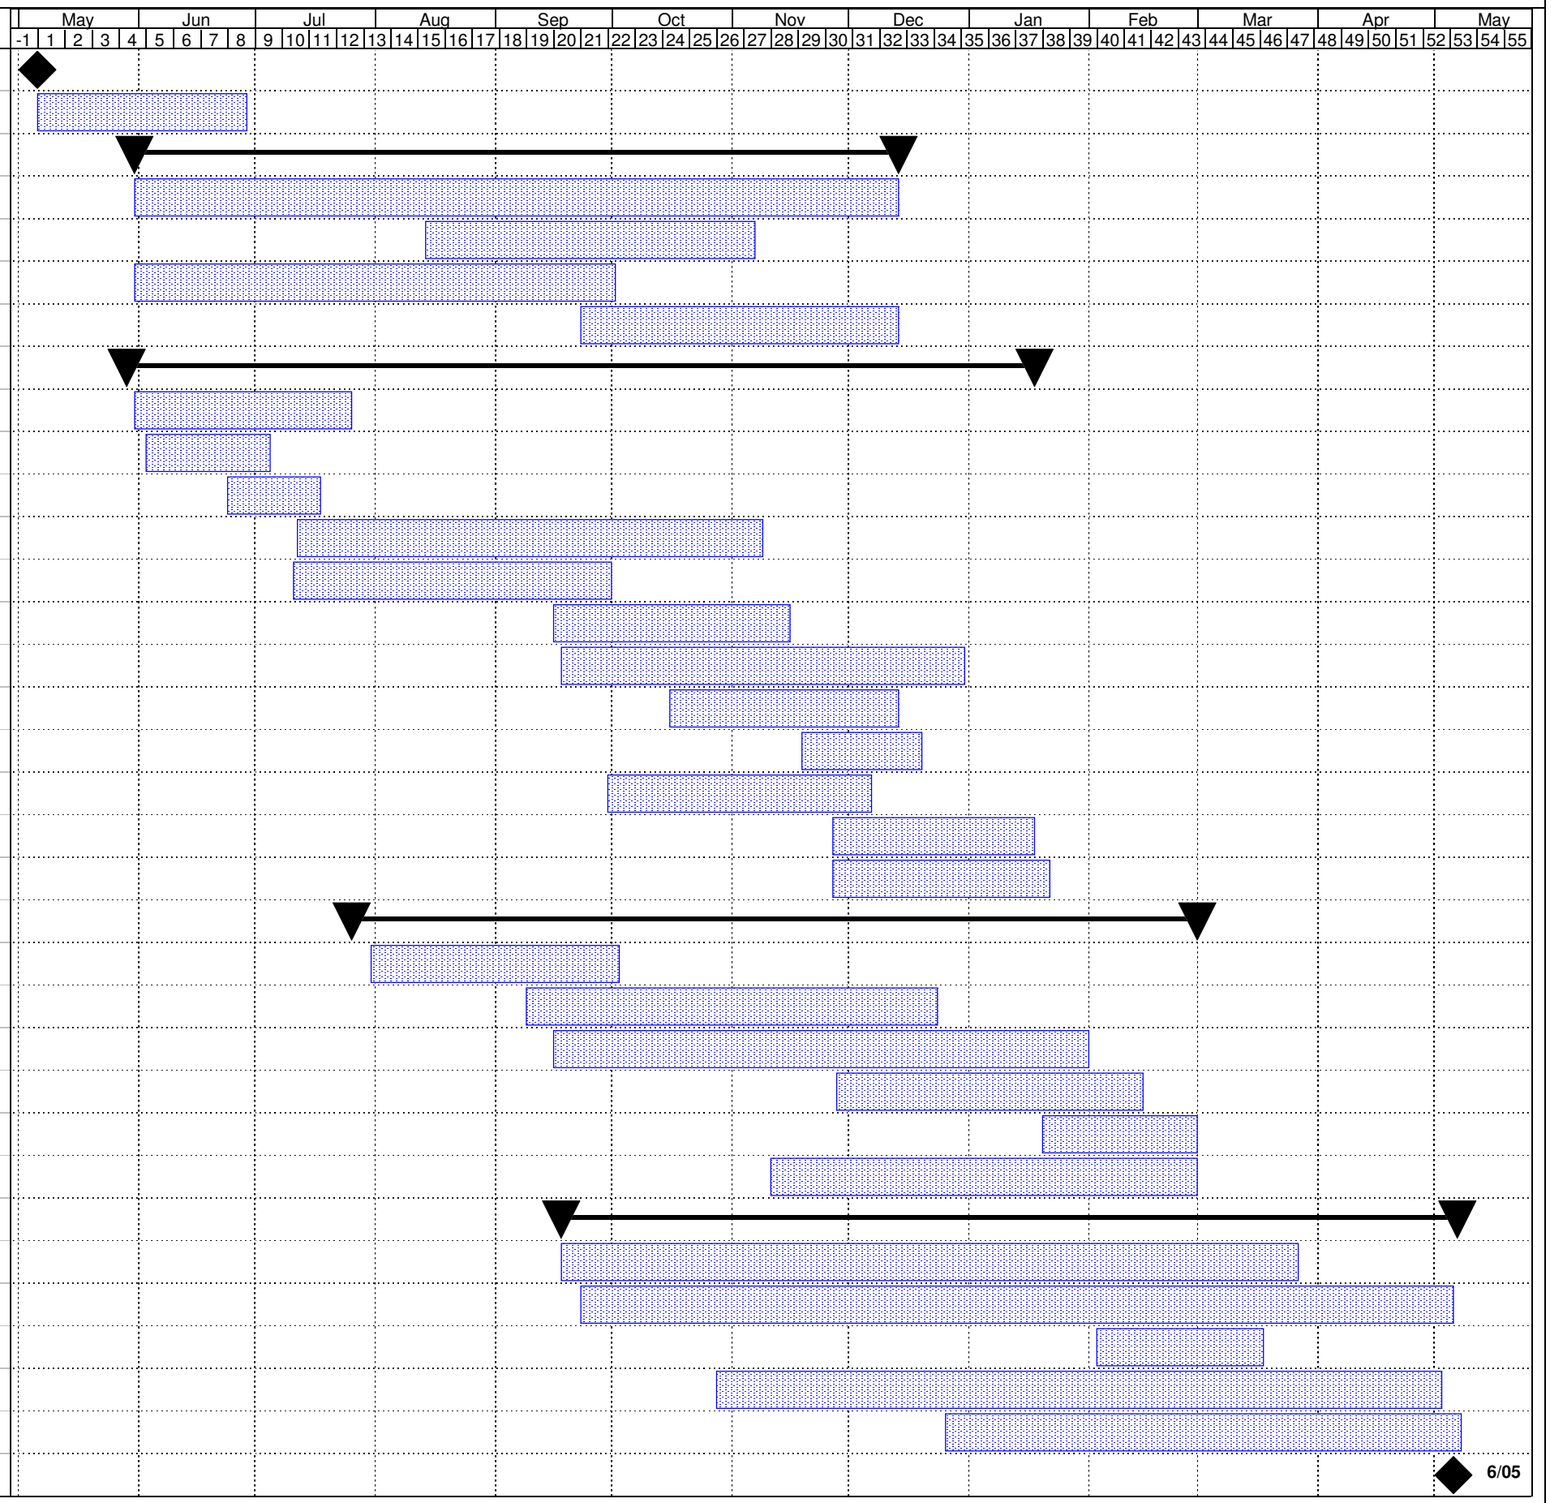

SOUTHERN CROSS ENGINEERING. PRELIMINARY PROJECT SCHEDULE
